


Upper Ohio - Scope



Placed in Service: 1936, Rehab: 1989

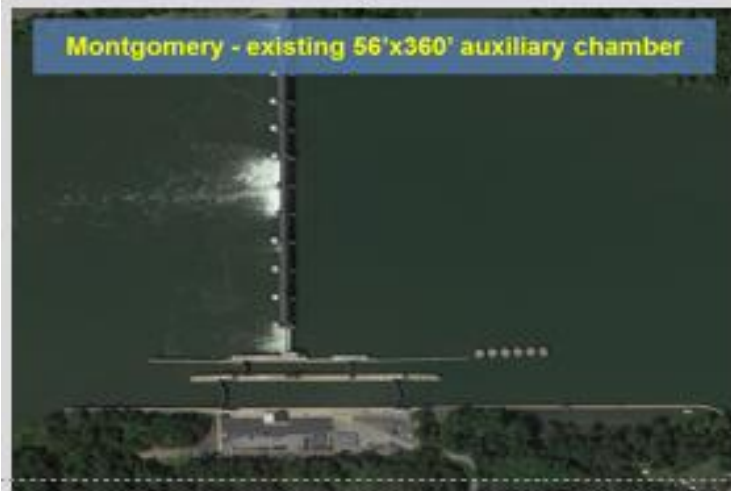

Placed in Service: 1929, Rehab: 1990



Placed in Service 1922, Rehab: 1986



BUILDING STRONG®
and Taking Care of People!

Upper Ohio - Project Status

1. Funding - Not in the FY17 or FY 18 President's Budget Request
 - Received \$5.525M in the FY17 work plan
 - Level III Economic Update
 - Geotechnical investigations – Montgomery Locks
 - Project Management Plan
 - Requesting \$8.795M in the FY18 work plan
 - Continue with Economic Update
 - As-Built surveys, VE Studies, Scope out Physical Navigation Model, Begin Physical and Numerical Models, Geotechnical investigations for Dashields, Preliminary design efforts
2. Level III Economic Update – Completion in May 2020
 - Reliability analysis
 - Demand forecasts and equilibrium traffic level determination
 - Transportation rate savings
 - Model loading, Calibration/Validation, Execute Model, and analysis
 - Reviews
